

ASHBURTON DISTRICT COUNCIL ROAD NETWORK MAINTENANCE AND OPERATIONS NEWSLETTER

ROAD0144 | Issue 45 | Oct 2024



Executive Summary

Tēnā koutou Katoa,

Our Heavy Maintenance Team continued with pre-reseal repair, completing all digouts that in the current reseal program. We will now focus on heavy maintenance sites as well as also targeting a few maintenance metalling sites.

Our Minor Maintenance teams continued to deliver excellent work this month, effectively responding to urgent Customer Request Management (CRM) tasks and completing scheduled work sites. Their main focus remained on footpath and drainage jobs, addressing both immediate and planned maintenance needs.

Our Cyclic Teams continued with pre-seal repairs, addressing potholes and edge breaks on reseal sites. In addition, they completed repairs on signage across the network, ensuring improved safety and visibility. Signs renewals and environmental maintenance were put on hold until budgets confirmed.

Our Trading Partners continued their commitment to maintaining the network, which involved sweeping and cleaning the streets, managing vegetation growth, performing line marking, and grading and maintaining unsealed roads.

James Faber
Contract Manager – Road Maintenance.

Summary below of key achievements during October:

- 614 potholes filled
- 280m Edge breaks repaired
- 2,569m² Digouts repaired
- 492km of routine grading completed
- 1,042m³ Maintenance Metalling
- 37 New signs installations/replacements completed
- 7 Soakpits Installed
- Line Marking – Rural

Completed Metalling Quantity for this Financial Year

- 33,724m³



Winslow Road after rain event.

Upcoming Planned Works – November 2024


Overview

Our Heavy Maintenance Team have completed all pre-reseal failures and will now focus on digout repairs. The teams will also target a few maintenance metalling sites that's in the area.

For November, we have scheduled footpath repairs and drainage works for our Minor Maintenance teams. Completion of this essential work is pending confirmation of the remaining budget.

Our Cyclic teams will continue with pre-reseal repairs.

Our supervisory team will be inspecting reseal sites to programme pre-reseal repairs and continue with all-faults and night-time inspections.

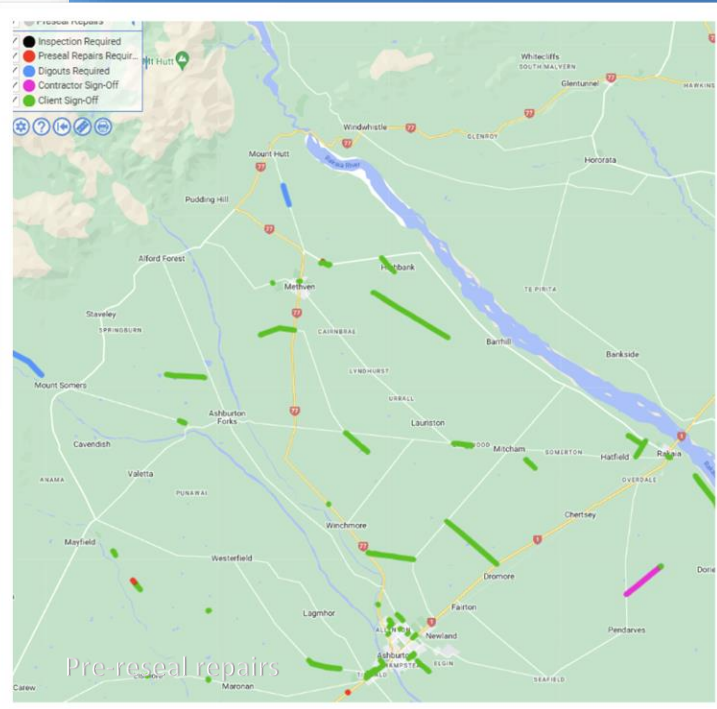

Summary of planned works

Maintenance Metalling – Withells Road & Lambies Road

Sealed Road Repairs – Ashburton Gorge Road, Chertsey Kyle Road, Gardiners Road, Haylers Road & Frasers Road

Footpath repair & replacement – Allison Street Road

Soak pit installation – Ashburton Stavely Road, Hills Road & Rawles Crossing Road

Sump Installation – Buckleys Terrace Road



Our Team
Working for You
Trading Partners



Tarbotton Land & Civil



Contact Us

Phone - 0800 HEBCAN
Email - ashburtonDC@heb.co.nz
Address – 203 Frasers Road, Tinwald
Web - www.heb.co.nz
